


ZME-D-904209-C001.DGN  
5/12/2010 10:28:23 AM beth cfr horley

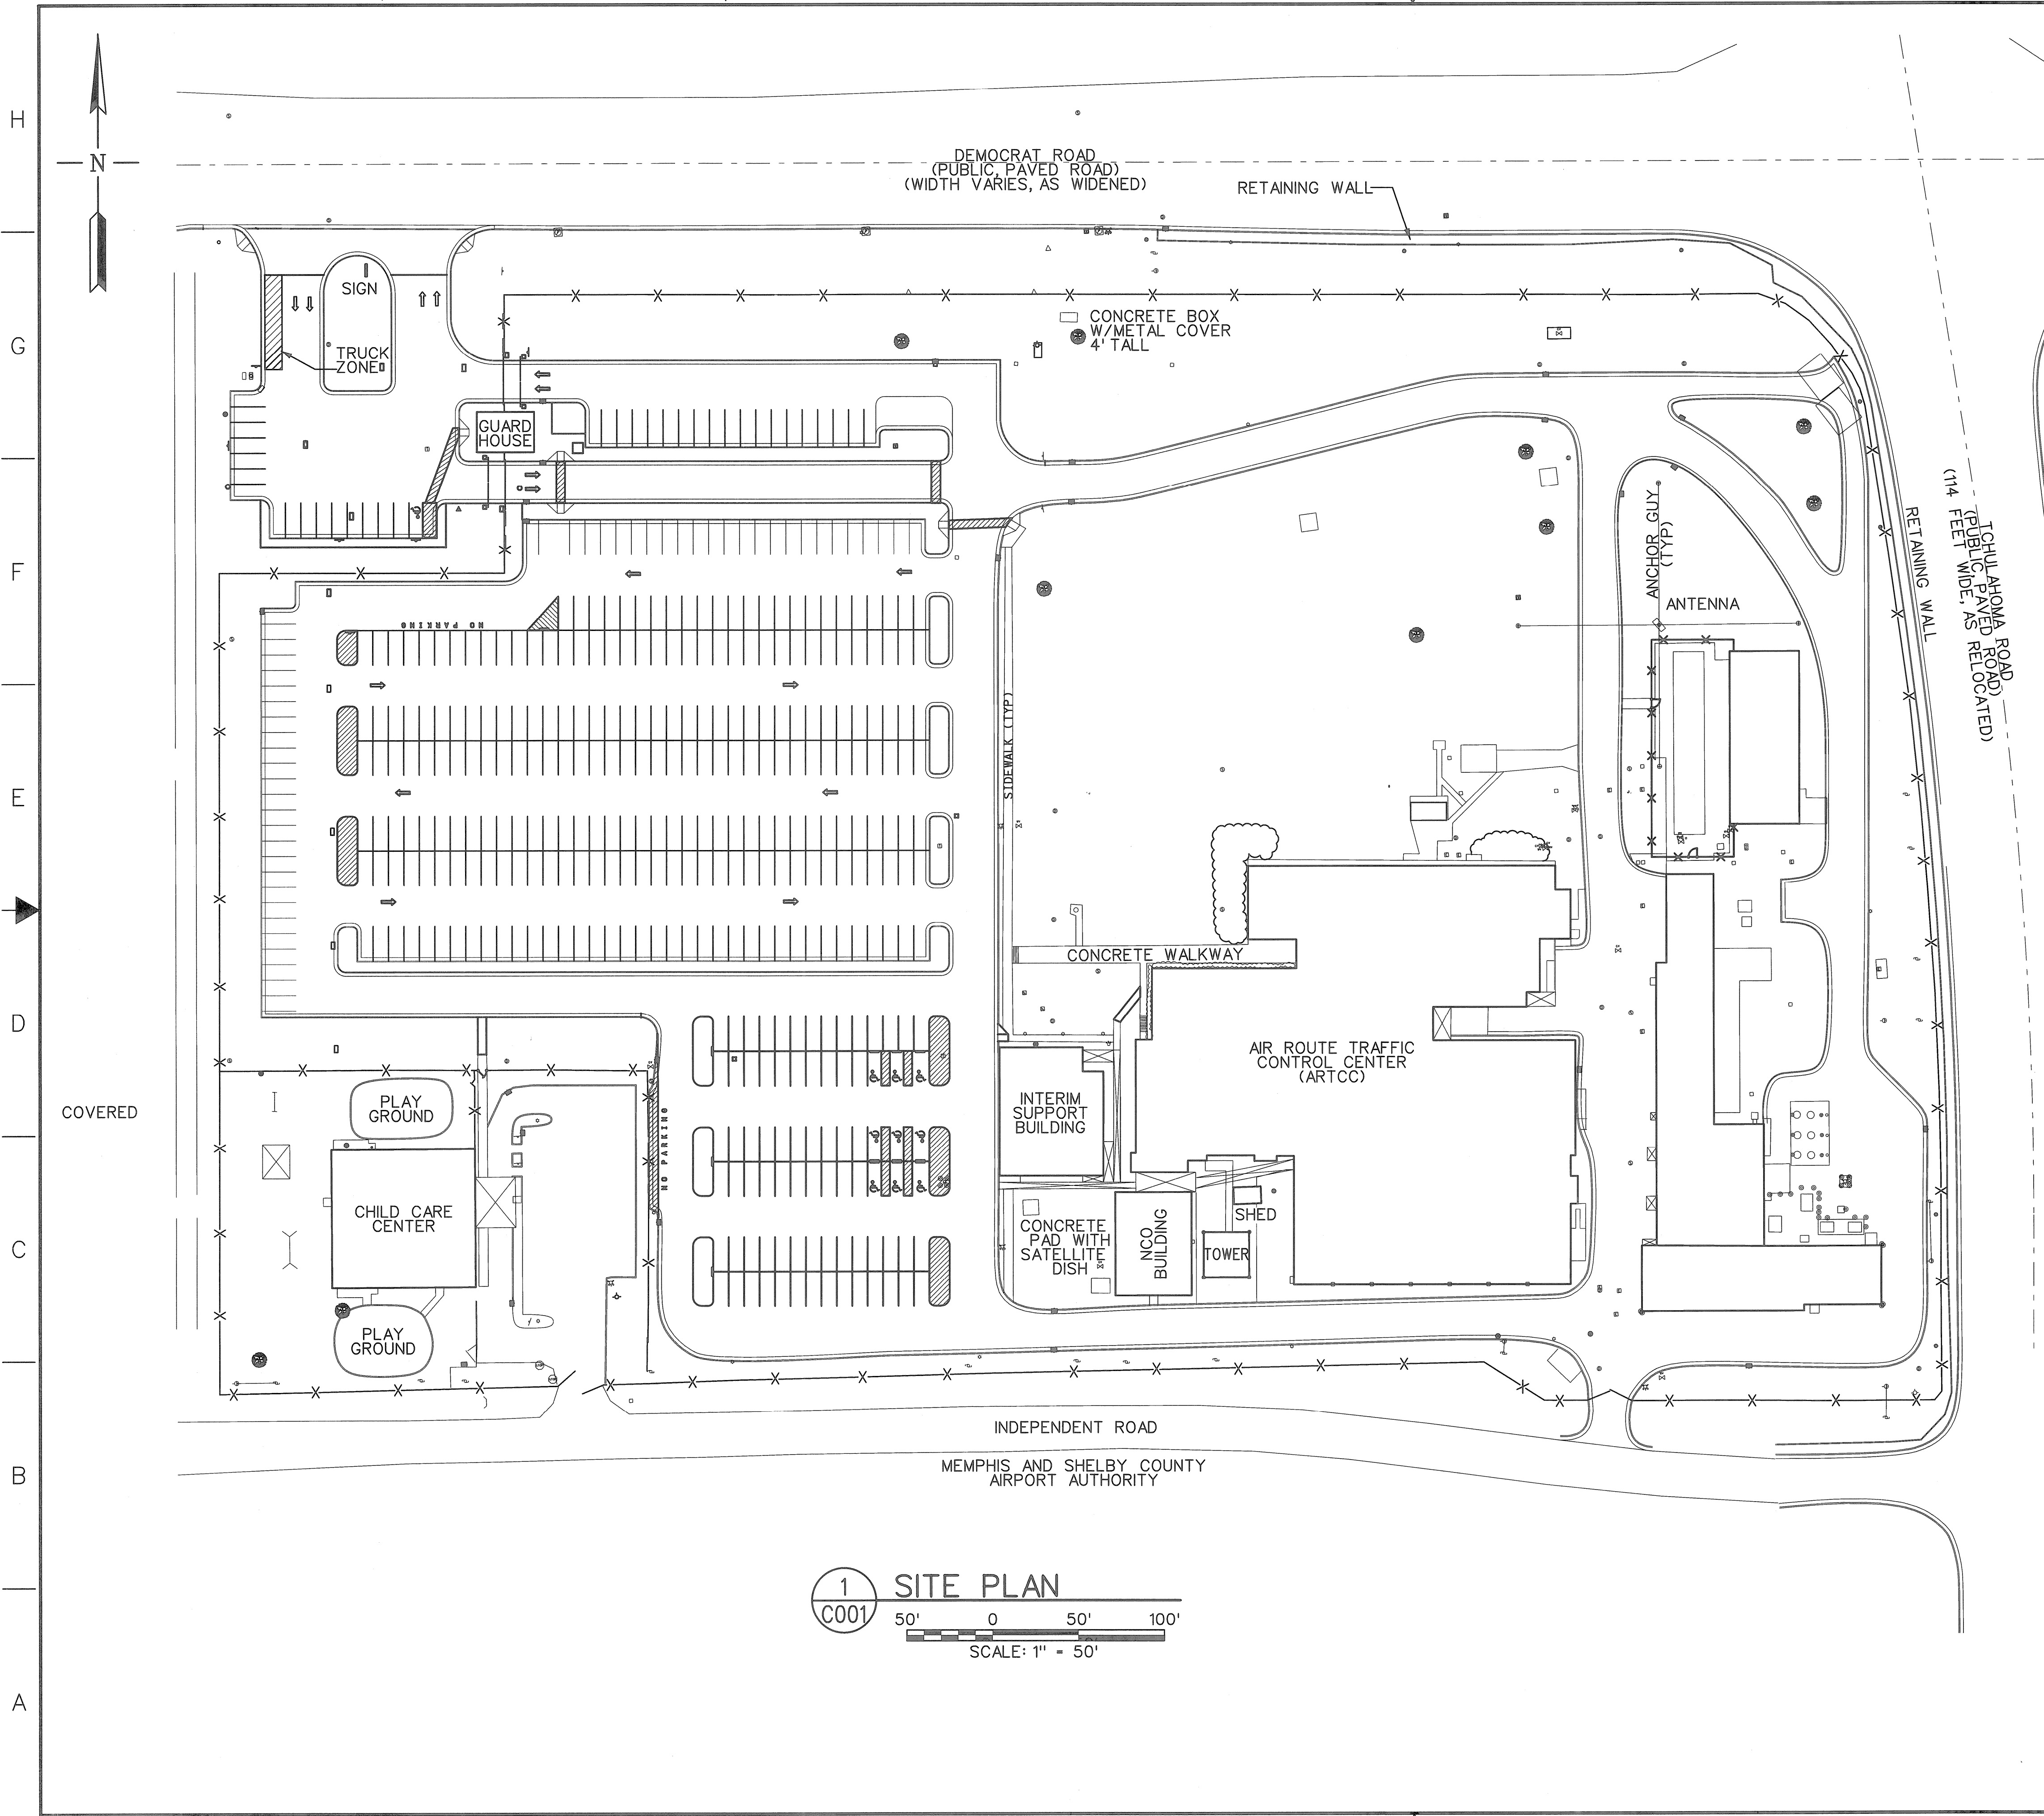

# CONSTRUCTION STAGING PLAN NOTES

THE FOLLOWING NOTES AND ACCOMPANYING "CONSTRUCTION STAGING PLAN" GRAPHICALLY REPRESENT MANY OF THE MAJOR REQUIREMENTS STATED IN "DIVISION 1- GENERAL REQUIREMENTS" OF THE SPECIFICATIONS. THESE NOTES PARAPHRASE DIVISION 1 REQUIREMENTS AND ARE NOT INTENDED TO MODIFY OR REPLACE ANY DIVISION 1 REQUIREMENTS. CONSTRUCTION ACCESS, CONTRACTORS PARKING, CONSTRUCTION OFFICES AND THE EXTENT/SIZE OF THE CONSTRUCTION STAGING AREA MUST BE COORDINATED WITH SITE PERSONNEL (VIA COR); PARTICULARLY IN CONJUNCTION WITH ONGOING PROJECTS. EACH PROJECT HAS THE SAME GENERAL REQUIREMENTS AND SITE PROBLEMS MAY PRECLUDE THE VARIOUS ALLOWANCES LISTED BELOW.

- A. CONSTRUCTION ACCESS.
- A.1 CONTRACTOR'S VEHICLES, PEDESTRIANS AND ALL DELIVERIES TO SITE SHALL BE THROUGH DEMOCRAT ROAD ENTRANCE.
- A.2 ALL DELIVERIES SHOULD BE SCHEDULED AT TIMES OTHER THAN THE FAA EMPLOYEE SHIFT CHANGES TO AVOID CONGESTION. FAA SHIFT CHANGES OCCUR AT 6:30 TO 8:00 A.M. AND AT 2:00 P.M. TO 4:00 P.M.
- A.3 PROVIDE SIGNAGE TO INDICATE THE ACCESS ROUTE FOR CONSTRUCTION EMPLOYEES AND DELIVERIES ON THE SITE. PROVIDE NECESSARY BARRICADES, LIGHTS, SIGNAGE AND FENCING TO PROTECT, WARN AND DIRECT ALL PERSONS NEAR THE CONSTRUCTION AREAS.
- B. CONTRACTOR PARKING.
- B.1 CONTRACTOR'S PERSONNEL PARKING SHALL BE COORDINATED WITH COR.
- C. FAA SECURITY REQUIREMENTS.
- C.1 AN ADVANCE LIST OF CONSTRUCTION PERSONNEL SHALL BE PROVIDED TO THE COR. SECURITY BADGES WILL BE ISSUED TO CONSTRUCTION PERSONNEL. ALL DELIVERIES SHALL BE SCHEDULED IN ADVANCE WITH COR. EACH CONSTRUCTION EMPLOYEE SHALL CHECK IN AND OUT AT THE MAIN SECURITY GATE.
- C.2 THE SITE IS A SECURE AREA AND ALL CONSTRUCTION PERSONNEL SHALL REMAIN IN THE CONSTRUCTION AREAS AT ALL TIMES.
- D. CONSTRUCTION MATERIAL STORAGE.
- D.1 STORAGE OF CONSTRUCTION MATERIAL AND TRAILERS ON THE SITE SHALL BE LIMITED TO THE CONSTRUCTION STAGING AREAS AS SHOWN ON THE CONSTRUCTION STAGING PLAN. MATERIALS SHALL BE NEATLY STORED AND PROTECTED AT ALL TIMES. A CONSTRUCTION FENCE MAY BE INSTALLED AT THE DISCRETION OF THE CONTRACTOR. CONTRACTOR SHALL NOT DIGGING WITHOUT PERMISSION FROM COR.
- E. CONSTRUCTION DEBRIS.
- E.1 DUMPSTERS FOR DISPOSAL OF CONSTRUCTION DEBRIS SHALL BE PROVIDED BY THE CONTRACTOR WITHIN THE STAGING AREAS. THE AREAS AROUND THE DUMPSTERS SHALL BE KEPT CLEAN AND FREE OF EXCESS DEBRIS DURING CONSTRUCTION. ALL DEBRIS SHALL BE REMOVED BY CONTRACTOR.
- G. CONSTRUCTION TOILET FACILITIES.
- G.1 PORTABLE CHEMICAL TOILETS SHALL BE PROVIDED BY THE CONTRACTOR WITHIN THE CONSTRUCTION STAGING AREAS.
- H. DEMOLITION AND CONSTRUCTION HOURS.
- H.1 SCHEDULE ALL NOISY DEMOLITION AND ALL OVERTIME CONSTRUCTION IN ADVANCE WITH THE COR.
- I. PARKING LOT AND DRIVEWAY REPAIR
- I.1 UPON COMPLETION OF WORK, THE CONTRACTOR SHALL REPAIR ALL PAVED SURFACES DAMAGED BY CONSTRUCTION ACTIVITIES TO ORIGINAL CONDITION.
- I.2 LAWN AREAS DISTURBED BY CONSTRUCTION ACTIVITY SHALL BE RESTORED TO ORIGINAL CONDITION.
- K. EQUIPMENT PROTECTION
- K.1 IT IS ABSOLUTELY MANDATORY THAT THE CONTRACTOR PROTECT ALL EXISTING FAA COMMUNICATION EQUIPMENT, ELECTRICAL AND MECHANICAL EQUIPMENT, OUTSIDE THE BUILDING FROM DAMAGE CAUSED BY IMPACT, WATER, OR DEBRIS.
- K.2 THE ARTCC IS A 24 HOUR 7 DAY PER WEEK OPERATING FACILITY. IT WILL BE NECESSARY TO COORDINATE ALL CONSTRUCTION ACTIVITY SO AS NOT TO INTERFERE WITH THE FUNCTIONS OF THE ARTCC.

REV	APPROVED DATE	DESCRIPTION	JCN	REDLINE DATE	APVD
DEPARTMENT OF TRANSPORTATION FEDERAL AVIATION ADMINISTRATION ATO - TECHNICAL OPERATIONS EASTERN SERVICE AREA ARTCC ADMINISTRATION WING BUILDING ROOF AREAS A, B AND C REPLACEMENT PROJECT SITE PLAN - STAGING					
MEMPHIS		MEMPHIS CENTER		TN	
REVIEWED BY	SUBMITTED BY	APPROVED BY			
	<i>Gregory D. Moore</i>	<i>[Signature]</i>			
DESIGNED	PROJECT/ENGINEER	MGR: ENGINEERING - ATLANTA			
DRAWN	DATE	DATE		JCN	
CHECKED	04/02/2010	04/02/2010		904209	
	ENGINEERING SERVICES	ENROUTE/FSS		REV	
ZME-D-904209-C001					

ISSUED FOR CONSTRUCTION
