

AMENDMENT OF SOLICITATION/MODIFICATION OF CONTRACT				1. CONTRACT ID CODE	PAGE	OF PAGES
2. AMENDMENT/MODIFICATION NO. 003		3. EFFECTIVE DATE 03/21/2011		4. REQUISITION/PURCHASE REQ. NO.		5. PROJECT NO. (If applicable)
6. ISSUED BY Federal Aviation Administration Acquisition Management Branch, ANM-52 1601 Lind Ave SW Renton, WA 98057				7. ADMINISTERED BY (If other than Item 6)		
8. NAME AND ADDRESS OF CONTRACTOR (No., street, county, State and ZIP Code)				9A. AMENDMENT OF SOLICITATION NO. DTFANM-11-R-00062		
				9B. DATED (SEE ITEM 11)		
				10A. MODIFICATION OF CONTRACT/ORDER NO.		
*TO BE COMPLETED BY VENDOR IF NOT COMPLETE				10B. DATED (SEE ITEM 13)		
CODE		FACILITY CODE				

11. THIS ITEM ONLY APPLIES TO AMENDMENTS OF SOLICITATIONS

☒ The above numbered solicitation is amended as set forth in Item 14. The hour and date specified for receipt of Offer is ☒ extended ☐ is not extended.

Offers must acknowledge receipt of this amendment prior to the hour and date specified in the solicitation on as amended, by one of the following methods:

(a) By completing Item 8 and 15, and returning 1 copies of the amendment; (b) acknowledging receipt of this amendment on each copy of the offer submitted; or (c) By separate letter or telegram which includes a reference to the solicitation and amendment numbers. FAILURE OF YOUR ACKNOWLEDGMENT TO BE RECEIVED AT THE PLACE DESIGNATED FOR RECEIPT OF OFFERS PRIOR TO THE HOUR AND DATE SPECIFIED MAY RESULT IN REJECTION OF YOUR OFFER. If by virtue of this amendment you desire to change an offer already submitted, such change may be made by telegram or letter, provided each telegram or letter makes reference to the solicitation and this amendment, and is received prior to the opening hours and date specified.

12. ACCOUNTING AND APPROPRIATION DATA (If required)

13. THIS ITEM APPLIES ONLY TO MODIFICATIONS OF CONTRACTS/ORDERS, IT MODIFIES THE CONTRACT/ORDER NO. AS DESCRIBED IN ITEM 14.

<input type="checkbox"/>	A. THIS CHANGE ORDER IS ISSUED PURSUANT TO: (Specify authority) THE CHANGES SET FORTH IN ITEM 14 ARE MADE IN THE CONTRACT/ORDER NO. IN ITEM 10A.
<input type="checkbox"/>	B. THE ABOVE NUMBERED CONTRACT/ORDER IS MODIFIED TO REFLECT THE ADMINISTRATIVE CHANGES (such as changes in paying office, appropriation data, etc.) SET FORTH IN ITEM 14.
<input type="checkbox"/>	C. THIS SUPPLEMENTAL AGREEMENT IS ENTERED INTO PURSUANT TO AUTHORITY OF:
<input type="checkbox"/>	D. OTHER (Specify type of modification and authority)

E. **IMPORTANT:** Contractor ☐ is not, ☒ is required to sign this document and return 1 copy to the issuing office.

14. DESCRIPTION OF AMENDMENT/MODIFICATION (Organized by UCF section headings, including solicitation/contract subject matter where feasible.)
THE ABOVE REFERENCED SOLICITATION FOR THE LOCKER ROOM RENOVATION AT THE DENVER ARTCC IS AMENDED AS FOLLOWS:

-SEE ATTACHED FOR ANSWER TO QUESTIONS.

-SEE ATTACHED DRAWING – LOCKER ROOM LAYOUT PLAN

DUE DATE FOR OFFERS HAS CHANGED TO : MARCH 25th 2011 AT 4PM PST.

ALL OTHER TERMS AND CONDITIONS REMAIN UNCHANGED.

Except as provided herein, all terms and conditions of the document referenced in Item 9A or 10A, as heretofore changed, remains unchanged and in full force and effect.

15A. NAME AND TITLE OF SIGNER (Type or print)		16A. NAME AND TITLE OF CONTRACTING OFFICER (Type or print) LELANIE RIVERA	
15B. CONTRACTOR/OFFEROR	15C. DATE SIGNED	16B. UNITED STATES OF AMERICA	16C. DATE SIGNED
(Signature of person authorized to sign)		BY (Signature of Contracting Officer)	

INSTRUCTIONS

Instructions for items other than those that are self-explanatory, are as follows:

(a) Item 1 (Contract ID Code). Insert the contract type identification code that appears in the title block of the contract being modified.

(b) Item 3 (Effective date).

(1) For a solicitation amendment, change order, or administrative change, the effective date shall be the issue date of the amendment, change order, or administrative change.

(2) For a supplemental agreement, the effective date shall be the date agreed to by the contracting parties.

(3) For a modification issued as an initial or confirming notice of termination for the convenience of the Government, the effective date and the modification number of the confirming notice shall be the same as the effective date and modification number of the initial notice.

(4) For a modification converting a termination for default to a termination for the convenience of the Government, the effective date shall be the same as the effective date of the termination for default.

(5) For a modification confirming the contracting officer's determination of the amount due in settlement of a contract termination, the effective date shall be the same as the effective date of the initial decision.

(c) Item 6 (Issued By). Insert the name and address of the issuing office. If applicable, insert the appropriate issuing office code in the code block.

(d) Item 8 (Name and Address of Contractor). For modifications to a contract or order, enter the contractor's name, address, and code as shown in the original contract or order, unless changed by this or a previous modification.

(e) Items 9, (Amendment of Solicitation No.- Dated), and 10, (Modification of Contract/Order No.- Dated). Check the appropriate box and in the corresponding blanks insert the number and date of the original solicitation, contract, or order.

(f) Item 12 (Accounting and Appropriation Data). When appropriate, indicate the impact of the modification on each affected accounting classification by inserting one of the following entries:

(1) Accounting classification
Net increase \$ _____

(2) Accounting classification
Net decrease \$ _____

NOTE: If there are changes to multiple accounting classifications that cannot be placed in block 12, insert an asterisk and the words "See continuation sheet."

(g) Item 13. Check the appropriate box to indicate the type of modification. Insert in the corresponding blank the authority under which the modification is issued. Check whether or not contractor must sign this document.

(h) Item 14 (Description of Amendment/Modification).

(1) Organize amendments or modifications under the appropriate Uniform Contract Format (UCF) section (if UCF used) headings from the applicable solicitation or contract. The UCF table of contents, however, shall not be set forth in this document.

(2) Indicate the impact of the modification on the overall total contract price by inserting one of the following entries:

(i) Total contract price increased by \$ _____

(ii) Total contract price decreased by \$ _____

(iii) Total contract price unchanged.

(3) State reason for modification.

(4) When removing, reinstating, or adding funds, identify the contract items and accounting classifications.

(5) When Template 11 is used to reflect a determination by the contracting officer of the amount due in settlement of a contract terminated for the convenience of the Government, the entry in Item 14 of the modification may be limited to -

(i) A reference to the letter determination; and

(ii) A statement of the net amount determined to be due in settlement of the contract.

(6) Include subject matter or short title of solicitation/contract where feasible.

(i) Item 16B. The contracting officer's signature is not required on solicitation amendments. The contracting officer's signature is normally affixed last on supplemental agreements.

RFO: DTFANM-11-R-00062

Locker Room Renovation at the Denver ARTCC in Longmont, CO

AMENDMENT 0003

****DUE DATE IS CHANGED TO MARCH 25th AT 4PM PT.****

QUESTION #1: In addenda #2 under the mechanical section item :

Sheet M001: HVAC Demolition – First Floor

Note 4 “Asbestos may be present. Take precaution including HEPA vac”

Are we to include asbestos removal? How much MAY be present?

ANSWER: *Any asbestos and abatement linked to the mechanical equipment would be handled as a change to the contract. Asbestos removal is not included in the mechanical (HVAC and piping) scope of work. If the mechanical contractor sees suspicious material in the pipe insulation around fittings, the contractor shall contact the Resident Engineer and stop work around the suspicious material until it can be tested and abated.*

QUESTION #2: We will need to cut into the HWS and HWR piping to remove the Fin Tube Radiator and cap as noted on the drawings. Do they know where the closest valves are that will allow us to shut this system down. Location of the valves and pipe sizing is necessary for us to know what is needed to drain and refill the system. It would also be helpful to know what type of Glycol they are using in the system, so we don't mix products.

ANSWER: *Actual isolation valve locations would have to be verified on-site during construction. According to the as-built drawings, the valves to be used to isolate the hot water supplying the area of renovation is located in the basement. These 2" diameter valves isolate hot water to AHU-320 and the fin tube radiators. The fin tube radiator piping is 1" diameter. ESU would know the actual glycol mixture if there is any.*

QUESTION #3: We are supposed to salvage and relocate one DDC Thermostat. We need to know the location of the DDC panel that this thermostat connects to. Is it located in the adjacent Mechanical Room or is it in another part of the complex?

ANSWER: *The DDC panel is located in the mechanical room.*



DEPARTMENT
OF
TRANSPORTATION




FEDERAL
AVIATION
ADMINISTRATION

LONGMONT, COLORADO
ZDV AIR ROUTE TRAFFIC CONTROL CENTER

LOCKER ROOM RENOVATION

DRAWING LIST

DRAWING NUMBER	DRAWING TITLE	DRAWING NUMBER	DRAWING TITLE
GENERAL		FIRE	
G001	COVER SHEET	F001	EXISTING FIRE SPRINKLER - FIRST FLOOR
G002	GENERAL ABBREVIATIONS	F002	FIRE SPRINKLER MOD - FIRST FLOOR
G003	LEGENDS		
G004	ELECTRICAL LEGEND	ELECTRICAL	
G005	MECHANICAL LEGEND	E001	POWER/PA AND SECURITY DEMOLITION PLAN
G006	CONSTRUCTION STAGING PLAN	E002	LIGHTING DEMOLITION PLAN
		E003	TELECOMMUNICATION DEMOLITION PLAN
ARCHITECTURAL		E004	FIRE DETECTION DEMOLITION PLAN
A001	FLOOR DEMOLITION	E005	NEW POWER & PA PLAN
A002	FLOOR PLAN	E006	NEW LIGHTING PLAN
A003	CEILING PLAN	E007	NEW FIRE DETECTION PLAN
A004	FINISH PLAN	E008	NEW TELECOMMUNICATIONS PLAN
A005	INTERIOR ELEVATIONS	E009	NEW SECURITY PLAN
A006	INTERIOR ELEVATIONS	E010	PANEL SCHEDULES (EXISTING)
A007	WALL SECTIONS & DETAILS	E011	PANEL SCHEDULES (UPDATED)
A008	WALL SECTIONS & DETAILS	E012	PARTIAL ONE-LINE DIAGRAM
A009	WALL SECTIONS & DETAILS	E013	TELECOMMUNICATION DETAILS
A010	WALL SECTIONS & DETAILS		
A011	WALL SECTIONS & DETAILS		
A012	AAS FIRST FLOOR REMODEL FINISH PLAN		
A013	LOCKER LAYOUT PLAN		
MECHANICAL			
M001	HVAC DEMOLITION - FIRST FLOOR		
M002	HVAC DEMOLITION - ABOVE CEILING		
M003	HVAC INSTALLATION - FIRST FLOOR		
M004	HVAC INSTALLATION - ABOVE CEILING		
M005	MECHANICAL SCHEDULE AND DETAILS		
M006	HVAC BALANCING		
M007	EXISTING AHU-300 CONTROL DIAGRAM		
M008	EXISTING AHU-320 CONTROL DIAGRAM		

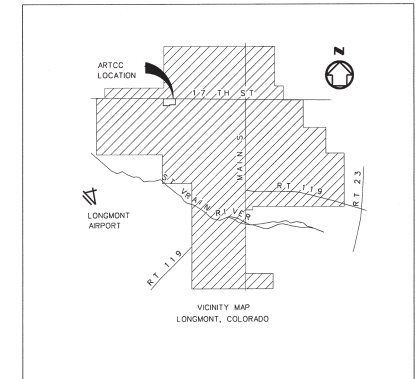

FOR OFFICIAL USE ONLY
PUBLIC AVAILABILITY TO BE DETERMINED UNDER 5 USC 552

REV	DATE	DESCRIPTION	JCN	RESOLINE DATE	APV
A	3/21/11	ADDED ZDV-907020-A013 TO DRAWING LIST	907020		

DEPARTMENT OF TRANSPORTATION
FEDERAL AVIATION ADMINISTRATION
ATO - TECHNICAL OPERATIONS WESTERN SERVICE AREA

ARTCC
LOCKER ROOM RENOVATION
COVER SHEET

DENVER LONGMONT CO


REVIEWED BY: *William Moreno Jr.* SUBMITTED BY: *William Moreno Jr.* APPROVED BY: *Dr. R. S. S. S.*

PROJECT ARCHITECT: *William Moreno Jr.* MGR: ENGINEERING - SEATTLE

DESIGNED: *WM* DATE: 01/10/2010 JCN: 907020

DRAWN: *FD* ENGINEERING SERVICES DRAWING NO: ZDV-907020-G001

CHECKED: *FD* ENROUTE

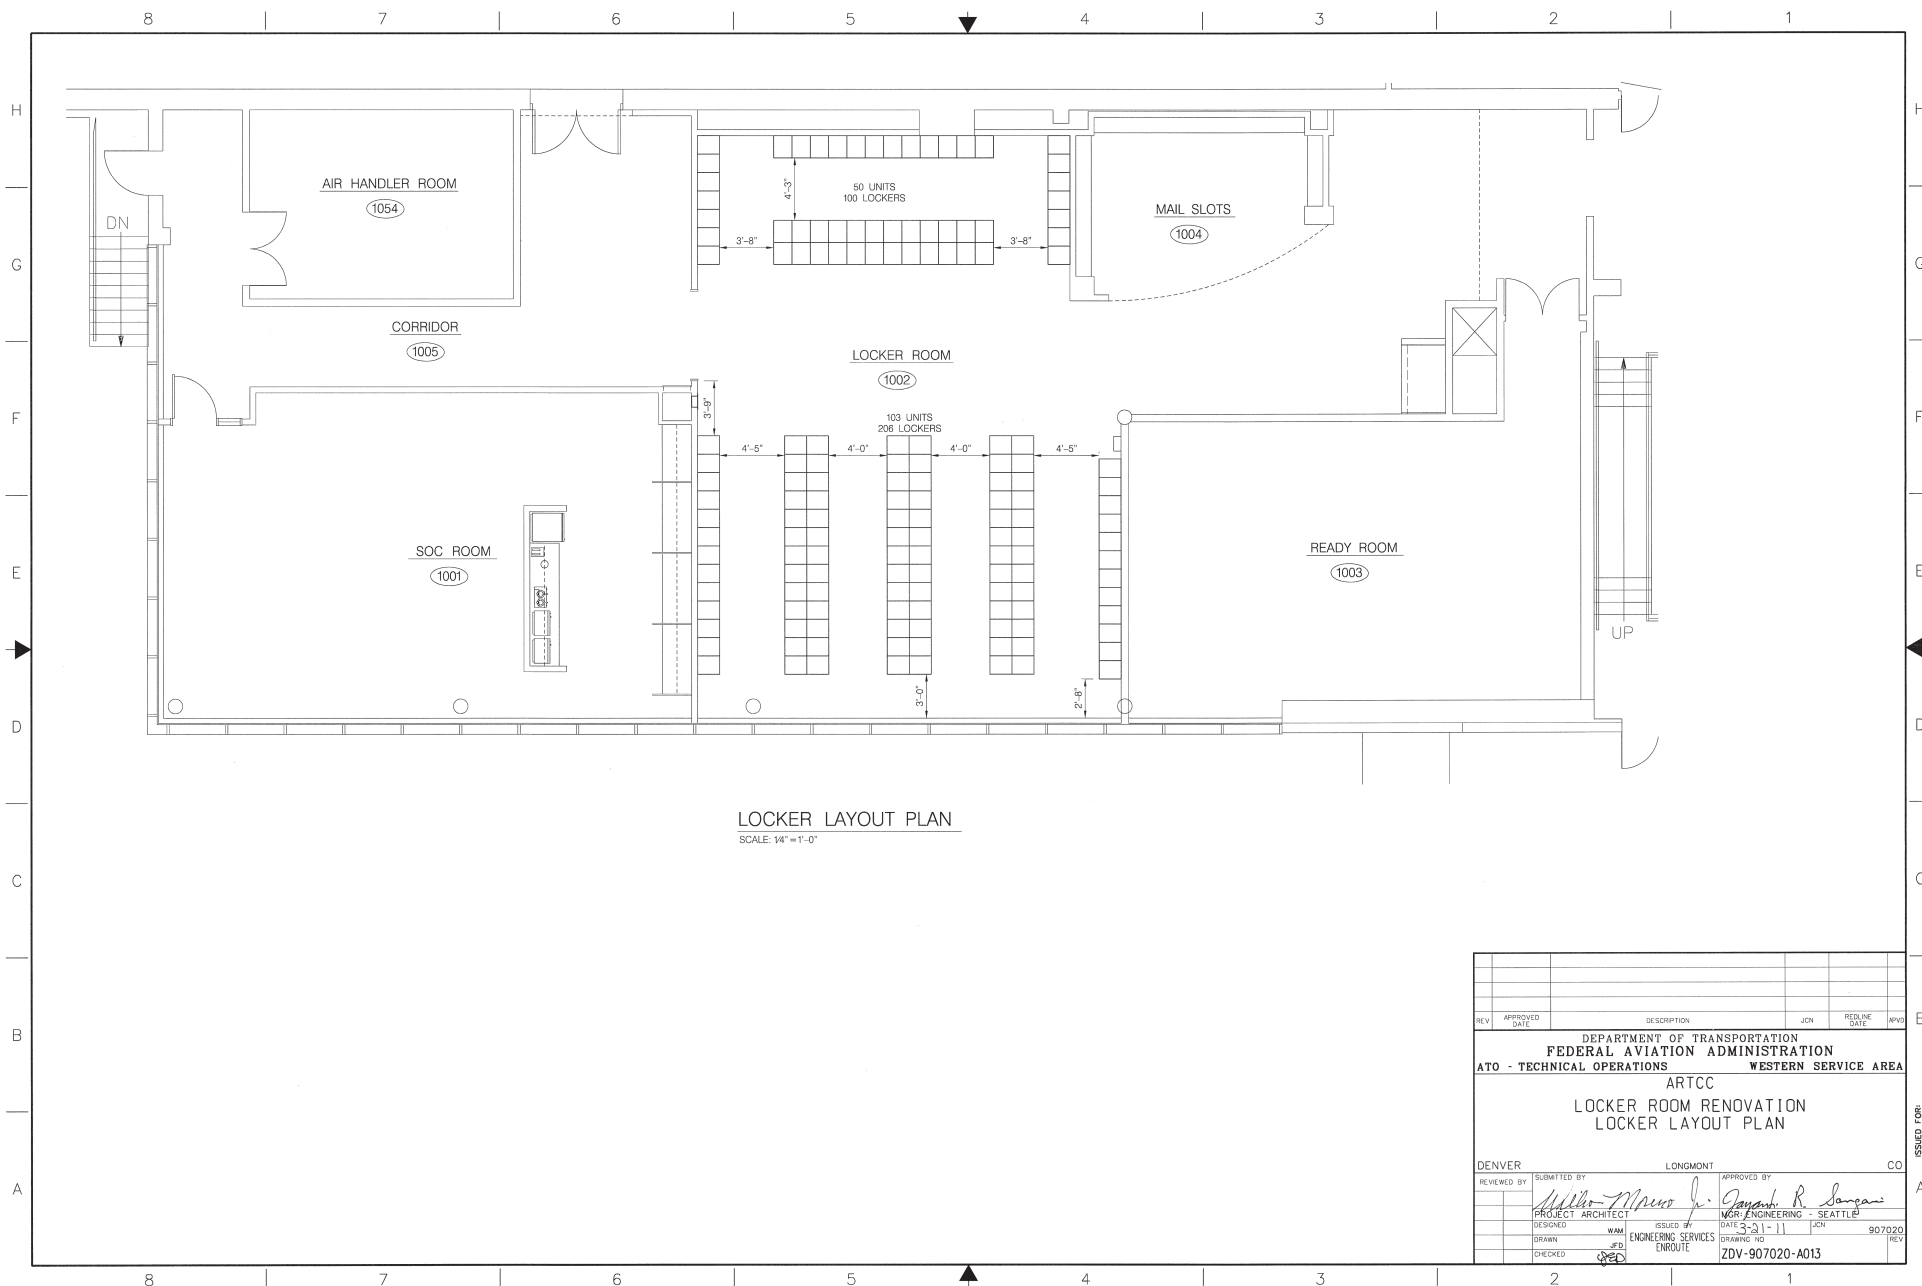

REV	APPROVED DATE	DESCRIPTION	JCN	REDLINE DATE	APV
DEPARTMENT OF TRANSPORTATION FEDERAL AVIATION ADMINISTRATION ATO - TECHNICAL OPERATIONS WESTERN SERVICE AREA ARTCC LOCKER ROOM RENOVATION LOCKER LAYOUT PLAN					
DENVER		LONGMONT		CO	
REVIEWED BY	SUBMITTED BY	APPROVED BY			
	<i>William Mauro Jr.</i>	<i>Raymond R. Sengani</i>			
PROJECT ARCHITECT	WAM	ISSUED BY	WEP ENGINEERING - SEATTLE		
DESIGNED	JFD	DATE	3-21-11	JCN	907020
DRAWN	JFD	ENGINEERING SERVICES	DRAWING NO		
CHECKED	JFD	ENDROUTE	DVDY-907020-A013	REV	

4-10-2020-011.dwg
 2/2/2011 9:35:58 AM
 jfd
